



Bobs Lake Dam – Construction Update

Update Points


- Introduction
- Construction Image Timeline
- Current Status and Next Steps





Introduction

- Construction was initiated in June 2018
- Two phase project with phase 1 now completed
- No major changes to date in project other than realignment of permanent access road

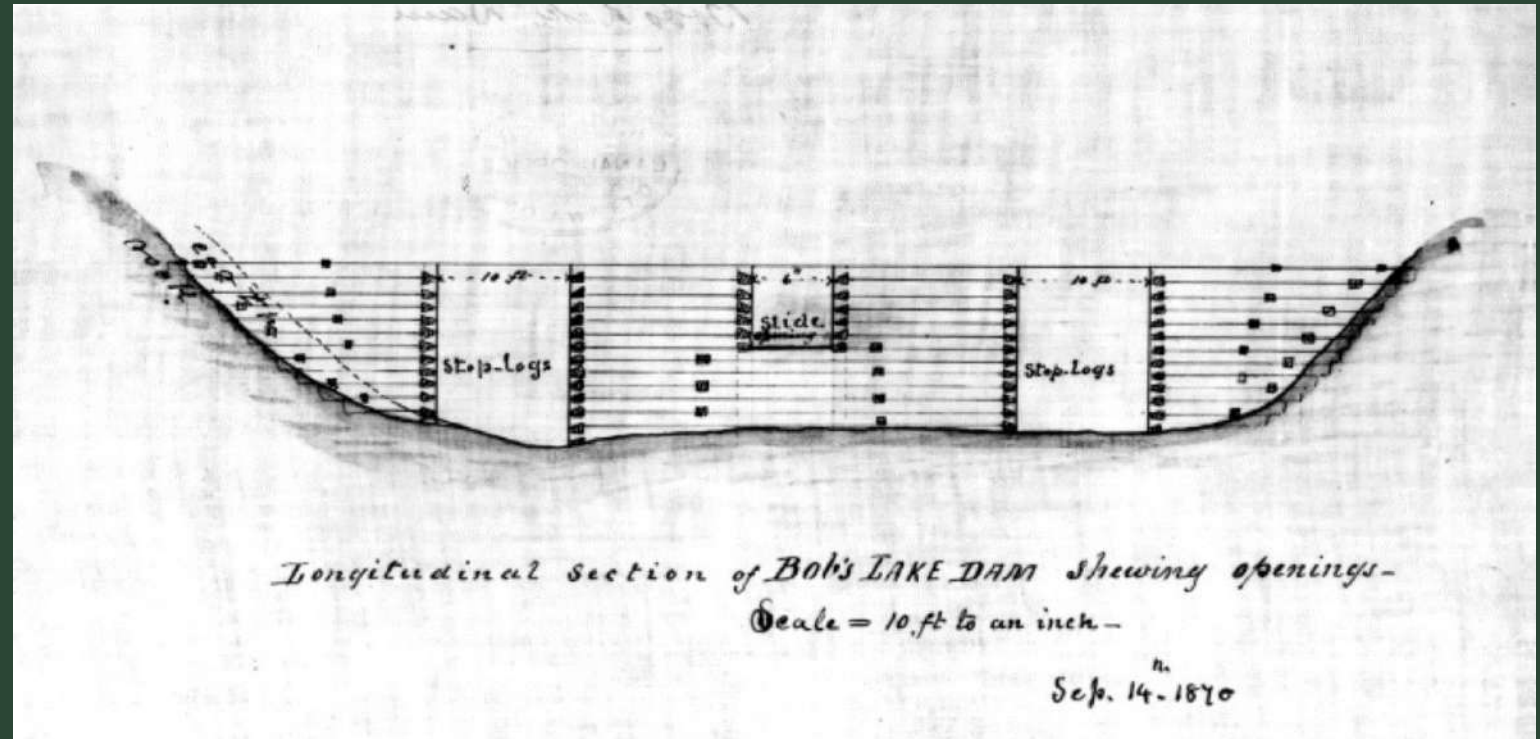



Construction Image Time Line – Access (Jun/Jul)





Construction Image Time Line – Cofferd Dam & Diversion (Jul/Aug)





Construction Image Time Line – Cofferd Dam & Diversion (Jul/Aug)





Construction Image Time Line – Excavation (Sep)





Construction Image Time Line – Excavation (Sep)





Construction Image Time Line – Rock Cleaning and Preparation (Sep/Oct)





Construction Image Time Line – Mud Mat & Shot Crete (Sep/Oct)





Construction Image Time Line – Grout (Oct/Nov)





Construction Image Time Line – First Concrete (20 Nov)





Construction Image Time Line – Concrete (Dec)





Construction Image Time Line – (Dec)





Construction Image Time Line – Phase 1 Concrete Completed







Current Status and Next Steps

Current Status

- Break in construction activity until spring
- Dam operations are at old dam until river bed rehabilitation work begins - control shifts to new dam

Next Steps

- Phase 2 construction of new dam
- Streambed rehabilitation
- Demolition of old dam
- Site restoration and access road construction



Questions

